



Dart Aerospace Ltd.
1270 Aberdeen St
Hawkesbury, ON
K6A 1K7
Canada

Tel (613) 632-5200

2

D119-796-141TRN
Job Sheet 174926



Part No: D119-796-141TRN

Job Qty: 1 ea

Part Name: Crosstube Turning Detail



Part Weight: 0 lbs

Status: Scheduled

Priority: Medium

Job Created: 3/23/18

Job Tracking No:

Due Date: 5/21/18

Created By: Michelle Gagnon-Donovan

Type: SOLD

Description:

Note: D119-796-141 REV H IPP REV A RQ 14/06/06 VERIFIED BY DD IPP REV:B 16.05.04 AS PER DWG REV.H DD VERF:JLM

Ship Via:

Bill of Materials

Job Routing

Op No	Operation	Qty	Start Date	Due Date	Standard		Workcenter/Supplier		Sign-off
					Setup hrs	Run Hrs	Workcenter / Supplier	Lead Time	
90	Start up Operation	1 Ea		5/19/18	0.00	0.00	Start Up Crosstubes-1		↑
100	Mori Seiki	1 pcs		5/19/18	1.99	1.52	Mori Seiki TL-40		DAS
110	QC	1 pcs		5/19/18	0.00	0.00	QC2		56
120	Mori Seiki	1 pcs		5/19/18	0.00	1.52	Mori Seiki TL-40		9-89
130	QC	1 pcs		5/19/18	0.00	0.00	QC2		↓
140	QC	1 pcs		5/19/18	0.00	0.00	QC8		JW GP
145	Crosstubes	1 pcs		5/19/18	0.00	0.33	Crosstubes-1		SA 18-04-18
150	HandFXtube	1 pcs		5/21/18	0.00	0.40	Crosstubes-3		
160	QC	1 pcs		5/21/18	0.00	0.00	QC7-1		LG014
170	Packaging	1 pcs		5/21/18	0.00	0.00	Packaging3-1		ms 18/04/18
180	QC21-FG	1 Ea		5/21/18	0.00	0.00	QC21		

Part Op 100 - 1-Fill tube with sand & install plugs on both ends as per Folio FB316 2-Turn first side as per Folio FB316 3-Blend Descriptions: transition lines only, **do not sand whole tube**: FOLIO REV: _____ DWG REV: _____ *Use mill bastard file, brush file repeatedly with file card. *Do not use sandpaper coarser than 320 grit.

120 - 1-Turn second side as per Folio FB316 2-Blend transition lines only, **do not sand whole tube**: 3-Remove sand and plugs 4- scribe batch # and part # as per dwg

145 - GRIND ONLY TRANSITION LINES SMOOTH LONGITUDE WAY.

150 - 1- handfinish X-TUBE INSIDE AND OUT 2- ALODINE AND ACID ETCH X-TUBE INSIDE AND OUT. USE RED SCOTCH BRITE

170 - LOCATION : LG014

Job BOM

Part / Item	Component Name	Quantity	Operation	Container
D6024-103	Crosstube Material	1 Ea (1 ea)	90-Start up Operation	

B150 732

Job Allocations

Operation	Component Part	Required	Inventory	Allocated
90-Start up Operation	D6024-103	1	30	0



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
CANADA
TEL.: 1 613 632-5200
Email: sales@dartaero.com
www.dartaerospace.com

Container No: S060634



Part: D119-796-141TRN

Job No: 174926

Serial No/Batch: S060634

Revision: H

Inspector:

Date: 04/12/18

26
2018

3/23/2018

[Dart Hawkesbury] Job Sheet - Gagnon-Donovan, Michelle

Part Specifications
Specifications could not be found.

Plex 3/23/18 9:40 AM Dart.Gagnon.Michelle

DART AEROSPACE LTD	Work Order:	174926
Description: Crosstube Assembly (AW119 MKII Fwd)	Part Number:	D119-796-141TRN
Inspection Dwg: D119-796-141 Rev: H		Page 1 of 2

FIRST ARTICLE INSPECTION CHECKLIST

Inspection Sheet Drawing Dimension		Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
SIDE A	6.00	+/-0.030	6.601	✓		VERNOX ↓	
	2.516	+/-0.005	2.518	✓			
	2.333	+0.005/-0.000	2.337	✓			
	2.333	+0.005/-0.000	2.337	✓			
	2.408	+0.005/-0.000	2.412	✓			
	2.502	+0.005/-0.000	2.507	✓			
	2.596	+0.005/-0.000	2.601	✓			
	2.596	+0.005/-0.000	2.601	✓			
SIDE B	6.00	+/-0.030	6.012	✓		↓	
	2.516	+/-0.005	2.518	✓			
	2.333	+0.005/-0.000	2.338	✓			
	2.333	+0.005/-0.000	2.338	✓			
	2.408	+0.005/-0.000	2.413	✓			
	2.502	+0.005/-0.000	2.507	✓			
	2.596	+0.005/-0.000	2.601	✓			
	2.596	+0.005/-0.000	2.601	✓			
	102.26	+/-0.020	102.26	✓		TAPE	

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE


QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation			Disposition		
			Completed By		
			Lead hand / Supervisor Approval Verification		
			QC / QA Coordinator Approval		
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER : ☐					

DART AEROSPACE LTD		Work Order: 174926
Description: Crosstube Assembly (AW119 MKII Fwd)		Part Number: D119-796-141TRN
Inspection Dwg: D119-796-141 Rev: H		Page 2 of 2

WALL THICKNESS MEASUREMENT

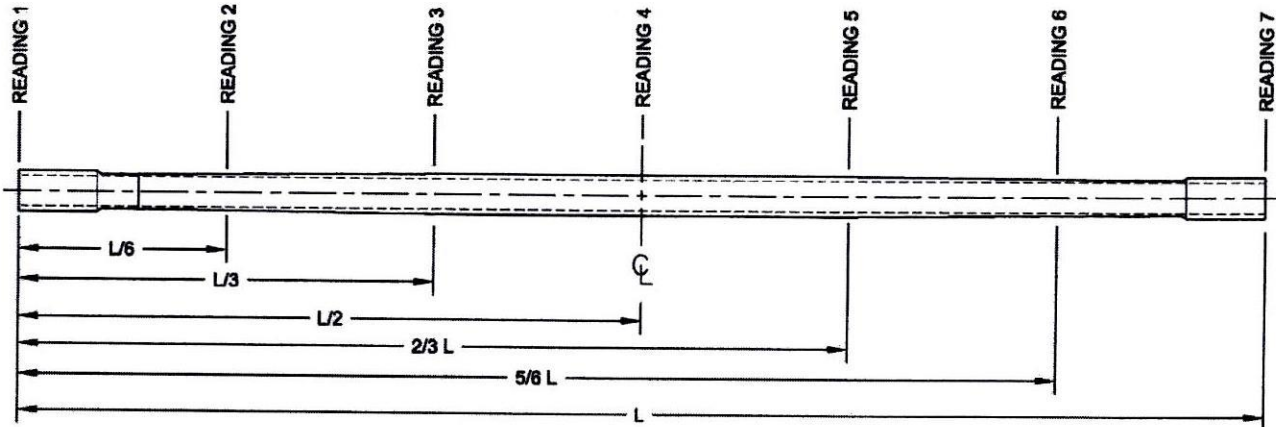

Location	WALL THICKNESS MEASUREMENT (IN)				Deviation Δw (max-min)	TOLERANCE
	w1	w2	w3	w4		
READING 1 L= 0"	261	258	254	257	.007	0.030"
READING 2 L= 17.04	185	173	180	191	.018	
READING 3 L= 34.09	271	261	268	280	.019	0.063"
READING 4 L= 51.13	310	299	289	297	.021	
READING 5 L= 68.17	273	270	266	271	.007	
READING 6 L= 85.22	182	181	182	185	.004	0.030"
READING 7 L= 102.26	262	257	254	259	.008	

Calibration Result

Actual Block Thickness: 200-300

Sitescan 250 Measured Thickness: 200 200

Measured by: DAS 56 9-89 Date: 2018-04-12	Audited by: TW Date: 18-04-16	Preliminary Approval: Date:
--	--	--

Rev	Date	Change	Revised by	Approved
A	15.04.14	New Issue (P/O D119-796-101)	KJ	
B	15.05.14	Tolerances revised per Dwg Rev G	KJ	
C	16.05.27	Dwg Rev updated	KJ	
D	16.09.13	Tolerance revised for Reading 3, 6 & 7	KJ	

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE



QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause				FAULT CATEGORY			
☐ Environment	☐ No Re-verification	☐ Pressure/Forced	☐ Temperature/Cure	☐ Power Loss/Surge	☐ Positioned Wrong		
☐ Design	☐ Operator	☐ Bending	☐ Set-up	☐ Folio/Program	☐ Outside Dimensions		
☐ Doc/Data	☐ Offset/Setup	☐ Centre Not Concentric	☐ BOM/Route	☐ Grain	☐ Over/Under tolerance		
☐ Equip/Tooling	☐ Supplier	☐ Cracks	☐ Broken/Damage/Defect	☐ Weld	☐ Part Incorrect		
☐ Handling/Pre	☐ Training	☐ Crimp/Kink/Ripple/Wave	☐ Inspection Incomplete/Unqualified	☐ Wrong Stock Pulled	☐ Part Lost/Missing		
☐ Material	☐ Use for Testing	☐ Cuffs	☐ Contamination	☐ Out of Sequence	☐ Part Moved		
☐ Internal Transport	☐ Poor Information	☐ Crushing	☐ Countersink	☐ Off-set	☐ Drawing		
☐ Tribal Knowledge	☐ Rushing	☐ Heat Treat	☐ Cut Too Short	☐ Mislabeled	☐ Finish		
☐ LOA	☐ Product Improvement	☐ Wave/Twist in Tube	☐ Instructions Incomplete/Unclear	☐ Fit/Function	☐ Misread		
☐ Substation	☐ Process Improvement	☐ Marks/Chatter	☐ Drill Holes	☐ Misaligned/off center	☐ Turning Sequence		
☐ Past Expiry Date	☐ Manufacturing Process	OTHER : _____					
☐ Misidentified	☐ Past Due						

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 174926
MAR 27 2018

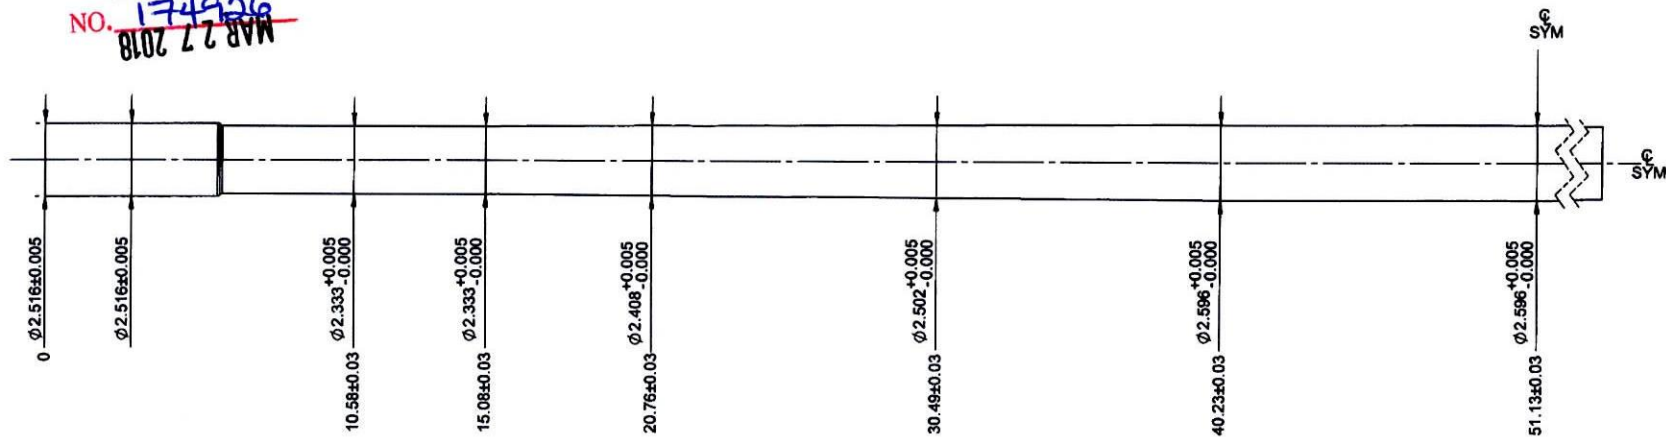

D119-796-141TRN CROSSTUBE, FWD

NOTES:

- 1) MATERIAL: MANUFACTURE FROM D6024-103 (PREFERRED) OR D6005-103
FINISHED LENGTH = 102.26 ± 0.020 (BEFORE BENDING/TRIMMING)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 16.70 lbs
- 8) PART IS SYMMETRICAL ABOUT CENTERLINE

RELEASED
2015-11-04

APPROVED

DESIGN	AP	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	AJS	DRAWING NO. D119-796-141	REV. H
MFG. APPR.	JLM	SHEET 5 OF 8	
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	XTUBE ASSY (AW119 MKII FWD)	NTS
DATE	15.10.13	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR REPRODUCED IN ANY FORM OR BY ANY MEANS WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

